

Weekly Construction Progress Report**IB & Tanks Decommissioning Project****Period:** Week Ending 4/12/2015**Project Work Performed:**

- No work performed on Monday, April 6, 2015 due to extended Holiday weekend.
- The Sheet Piling contractor mobilized to the site on Tuesday, April 7, 2015. Additional equipment (crane) and materials arrived throughout the week.
- Sheet piling was delivered to the site and the crane was assembled on-site in preparation of sheet pile installation.
- Additional "obstructions" including overhead piping was removed in preparation for sheet piling and sprung structure installation.
- On Friday, April 10, 2015, installation of the sheet piling was initiated in the northwest corner of the IB.
- Continued relocation of the soil stockpile in the area west of the IB.
- Sodium permanganate was applied to the sludge in the IB in order to reduce potential vapors during sheet piling activities.
- Baseline perimeter air monitoring activities were continued. Beginning Friday, construction related air monitoring was performed in conjunction with sheet piling activities.

Work Projected Next Week:

- Continue relocation of soil stockpile. Install erosion control measures around relocated stockpile.
- Continue the removal of overhead obstructions.
- Continue to advance sheet piles around the perimeter of the IB area.
- Continue site preparation activities for sprung structure around the IB.
- Begin preparations for installation of sprung structure blower units, electrical contractor meetings.
- Potentially mobilize personnel and equipment for installation of the water treatment system

Action Items:

- TCLP analytical to be completed for CKD, off-site backfill

Solids Production:

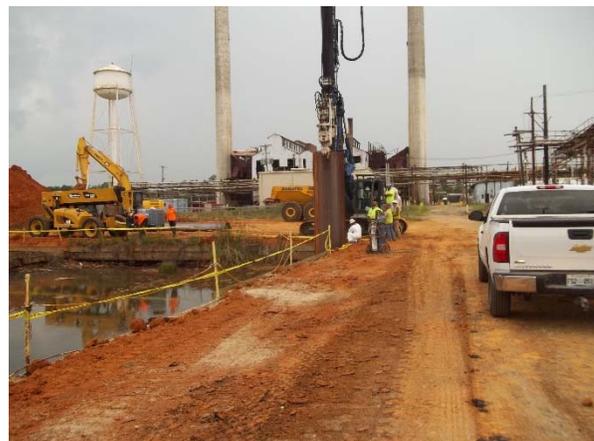
- None

Water Production:

- None

Air/Odor Monitoring

- Baseline air monitoring was completed each day during the week ending on Thursday 4/9/2015.
- Project related air monitoring was initiated Friday, prior to sheet pile installation activities.

Hercules Plant**Hattiesburg, MS****Unloading of sheet piles****Soil relocation and sheet piling activities****Installation of sheet piles at the northwest corner of the IB**
